

Lennox® S40 Smart Thermostat

Troubleshooting & Checkout Sheet

Job Name: _____ Date: _____
Address: _____ Phone: _____
City: _____ State: _____ Zip: _____

Company Name _____ Company Phone: _____
Technician: _____ Technician Cell: _____
Dealer # _____


Complaint/Symptoms/Visual Inspection (Details, don't leave anything out, pictures can also be very beneficial when reporting an issue, use last page for additional space if needed)

Equipment Information


	Outdoor Unit	Indoor Coil	Furnace (or Blower Coil)	Accessory	Thermostat
Manufacturer					
Model #					
Serial #					
Date Installed					
Lineset Length: _____ Rise: _____ Suction Line Size: _____ Liquid Line Size: _____					Number of Elbows: _____
Indoor Coil is ☐ Above ☐ Below ☐ Same Level as Outdoor Unit Matched System yes no (circle one)					

Circle the wiring scenario that best fits your application below.
If your wiring application is different, please describe here.


(Using shielded wiring for Communication Lines)

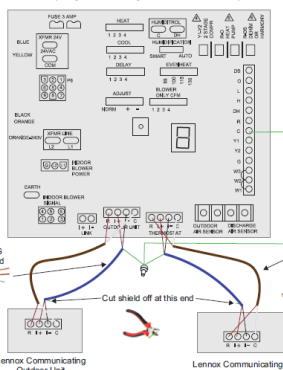


Indoor Unit Communicating Control
(Using 2-conductor Unshielded Cable for Communication Lines and Separate 2-conductor Unshielded Cable for R and C)

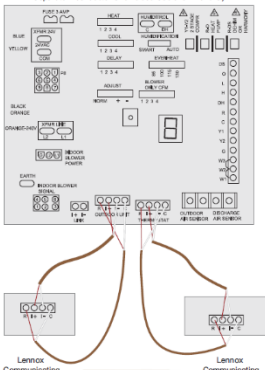

Indoor Unit Controller

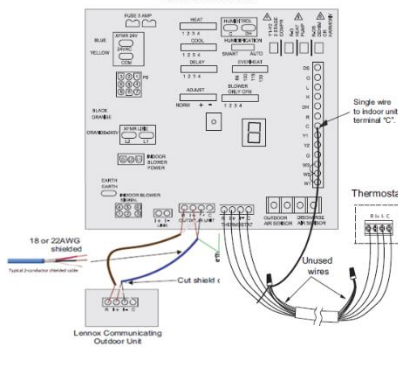

Indoor Unit Controller

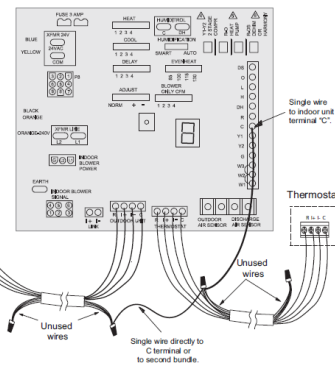

Installation Checklist

Thermostat Checks:		YES	NO
1	Is the Thermostat properly placed and connected to wall plate?		
2	Are all terminal wiring properly connected and tight on wall plate?		
3	Is the screen blank after initial power-up? The Thermostat may take up to three minutes before anything appears on the screen due to a Thermostat low battery condition. Thermostat battery charging only occurs when connected to the sub-base.		
4	When required, is either or both the discharge (DATS) and outdoor air temperature (OATS) sensors properly connected and isolated when used?		
System Checks:		YES	NO
1	Is the Wi-Fi connected?		
2	Has the homeowner downloaded the Lennox Thermostat application from either Google Play or IOS App Store to their mobile devices?		
3	Is the Lennox Dealer account number or your main shop phone number been added to the dealer information screen?		
4	If applicable, has the air handler's electric heat strips been commissioned? If not, commissioning of heat strips must be performed.		
5	Has a complete system test been run? If not, from the Thermostat home screen go to Settings > Advance Settings > View Support Service Control Center > and select Tests.		

Are there any accessories? Please circle all that apply.

Humidifier Dehumidifier Float/Wet Switches ERV/HRV Lennox Ventilator Pure Air S Other__

Are accessories wired per the S40 Installation & Setup Guide? YES NO

Are accessories isolated with the use of a relay? YES NO

Is this a Dual Fuel Application? YES NO

Is Balance Point Control Enabled? YES NO NA

What are the Balance Points? LOW _____ HIGH _____ NA

Is Humidification Enabled? YES NO **Setpoint** _____%

Is Dehumidification Enabled? YES NO **Setpoint** _____%

Air Volumes? Cooling _____ Heating _____ HP Heating _____ Cont. _____

Voltage Checks

At Thermostat R-C _____ VAC **I+ - C** _____ VDC **I- - C** _____ VDC

At ID Board R-C _____ VAC **I+ - C** _____ VDC **I- - C** _____ VDC

At OD Board R-C _____ VAC **I+ - C** _____ VDC **I- - C** _____ VDC

Checking for voltage bleed

Inductive Voltage into the Communication Buss will cause Communication Errors!

With only R connected at ID Board (See Diagram Below), what are the voltage readings on all disconnected wires to 24v Common

You should have no more than .7 VAC on any wire!

Outdoor Unit - Wire 1 ____ 2 ____ 3 ____ 4 ____ 5 ____ 6 ____ 7 ____

Same Check for Thermostat - Wire 1 ____ 2 ____ 3 ____ 4 ____ 5 ____ 6 ____ 7 ____

